



ID	Task Mode	Task Name	Start	Duration	Finish	Predecessors	1, '19	Sep 8, '19	Sep 15, '19	Sep 22, '19	Sep 29, '19	Oct 6, '19	Oct 13, '19	Oct 20, '19	Oct 27, '19	Nov 3, '19	Nov 10, '19	Nov 17, '19	Nov 24, '19	Dec 1, '19	Dec 8, '19	Dec 15, '19	Dec 22, '19	Dec 29, '19	Jan 5, '20	Jan 12, '20	Jan 19, '20	Jan 26, '20	Feb 2, '20	Feb 9, '20						
1		PE Pool & Dive Platform Repair and Natatorium Improvements	Thu 9/5/19	260 days?	Sat 9/5/20		PE Pool & Dive Platform Repair and Natatorium Improvements																													
2		Design Professional Selection & Contract	Thu 9/5/19	55 days?	Wed 11/20/19		Design Professional Selection & Contract																													
3		Prepare A/E RFQ	Thu 9/5/19	3 days?	Mon 9/9/19		Prepare A/E RFQ																													
4		Submit RFQ - OFCC	Tue 9/10/19	1 day	Tue 9/10/19	3	Submit RFQ - OFCC																													
5		A/E RFQ Advertisement	Wed 9/11/19	29 edays	Thu 10/10/19	4FS+1 day	A/E RFQ Advertisement																													
6		Pre-Proposal Meeting / Site Visit	Thu 9/26/19	1 day?	Thu 9/26/19	5SS+2 wks	Pre-Proposal Meeting / Site Visit																													
7		Qualifications Due	Thu 10/10/19	0 days	Thu 10/10/19	5	Qualifications Due																													
8		Search Committee Review & Shortlist	Mon 10/14/19	10 edays	Thu 10/24/19	7FS+3 days	Search Committee Review & Shortlist																													
9		Search Committee Meeting	Fri 10/25/19	1 day	Fri 10/25/19	8	Search Committee Meeting																													
10		Shortlist Interviews & Final Selection	Tue 11/5/19	1 day	Tue 11/5/19	9FS+10 edays	Shortlist Interviews & Final Selection																													
11		Contract Negotiation/ Fee Proposal	Wed 11/6/19	6 edays	Tue 11/12/19	10FS+1 day	Contract Negotiation/ Fee Proposal																													
12		A/E CSU PO Issued	Tue 11/12/19	3 days	Fri 11/15/19	11	A/E CSU PO Issued																													
13		Attorney General - Execute A/E Contract	Mon 11/18/19	3 days	Wed 11/20/19	12	Attorney General - Execute A/E Contract																													
14		Programing/Design Phase/ Construction Documents	Mon 11/25/19	97 days?	Fri 4/10/20		Programing/Design Phase/ Construction Documents																													
15		Programing/ Scope Development	Mon 11/25/19	1.5 ewks	Fri 12/6/19	13FS+3 days	Programing/ Scope Development																													
16		Schematic Design	Fri 12/6/19	2.5 ewks	Mon 12/23/19	15	Schematic Design																													
17		Cost Estimate 1	Fri 12/20/19	5 edays?	Wed 12/25/19	16FS-2 days	Cost Estimate 1																													
18		Holiday Break	Thu 12/26/19	6 days	Fri 1/3/20	17	Holiday Break																													
19		CSU Review	Mon 1/6/20	3 days	Wed 1/8/20	18	CSU Review																													
20		Design Development	Thu 1/9/20	4 ewks	Thu 2/6/20	19FS+1 day	Design Development																													
21		Cost Estimate 2	Wed 2/5/20	5 edays	Mon 2/10/20	20FS-2 days	Cost Estimate 2																													
22		CSU Review	Mon 2/10/20	3 days	Wed 2/12/20	21	CSU Review																													
23		Construction Documents	Wed 2/12/20	4 ewks	Wed 3/11/20	22	Construction Documents																													
24		Permit/ Plan Review	Wed 3/11/20	30 edays?	Fri 4/10/20	23	Permit/ Plan Review																													
25		Advertisement, Bidding Contract Award	Mon 3/9/20	27 days?	Tue 4/14/20		Advertisement, Bidding Contract Award																													
26		Advertisement 1	Mon 3/9/20	1 day?	Mon 3/9/20	23FS-3 days	Advertisement 1																													
27		Advertisement 2	Mon 3/16/20	1 day?	Mon 3/16/20	26FS+6 edays	Advertisement 2																													
28		Pre-Bid Meeting / Site Visit	Thu 3/19/20	1 day?	Thu 3/19/20	26SS+10 edays	Pre-Bid Meeting / Site Visit																													
29		Advertisement 3	Mon 3/23/20	1 day?	Mon 3/23/20	27FS+6 edays	Advertisement 3																													
30		Bids Due	Tue 3/31/20	1 day?	Tue 3/31/20	29FS+7 edays	Bids Due																													
31		Scope Review	Thu 4/2/20	1 day?	Thu 4/2/20	30FS+1 day	Scope Review																													
32		Issue PO	Mon 4/6/20	3 days	Wed 4/8/20	31FS+1 day	Issue PO																													
33		Attorney General - Execute GC Contract	Fri 4/10/20	3 days	Tue 4/14/20	32FS+1 day	Attorney General - Execute GC Contract																													
34		Construction	Fri 4/24/20	96 days?	Sat 9/5/20		Construction																													
35		Construction	Fri 4/24/20	3.5 mons	Thu 7/30/20	33FS+7 days	Construction																													
36		Pool Refill and Treatment	Mon 7/27/20	7 days	Tue 8/4/20	35FS-4 days	Pool Refill and Treatment																													
37		Owner Move in Occupancy	Mon 8/3/20	1 day?	Mon 8/3/20	35FS+1 day	Owner Move in Occupancy																													
38		Fall Semester Start	Sat 8/22/20	1 day	Sat 8/22/20		Fall Semester Start																													
39		A/E-CMR Closeout Contracts Complete	Wed 7/22/20	1.5 emons	Sat 9/5/20	35FS-7 days	A/E-CMR Closeout Contracts Complete																													
40		Academic Calendar	Sat 5/18/19	575 days?	Sat 12/12/20		Academic Calendar																													
1		Summer Semester 2019	Sat 5/18/19	84 days?	Fri 8/9/19		Summer Semester 2019																													
2		Fall Semester 2019	Sat 8/24/19	113 days?	Sat 12/14/19		Fall Semester 2019																													
3		Spring Semester 2020	Sat 1/11/20	119 days?	Fri 5/8/20		Spring Semester 2020																													
4		Summer Semester 2020	Sat 5/16/20	84 days?	Fri 8/7/20		Summer Semester 2020																													
5		Fall Semester 2020	Sat 8/22/20	113 days?	Sat 12/12/20		Fall Semester 2020																													

Critical Critical Progress Split Manual Task Finish-only Baseline Summary Progress Manual Summary External Tasks Inactive Task Inactive Summary
Critical Split Task Task Progress Start-only Duration-only Baseline Split Summary Project Summary External Milestone Inactive Milestone Deadline

20	Feb 16, '20	Feb 23, '20	Mar 1, '20	Mar 8, '20	Mar 15, '20	Mar 22, '20	Mar 29, '20	Apr 5, '20	Apr 12, '20	Apr 19, '20	Apr 26, '20	May 3, '20	May 10, '20	May 17, '20	May 24, '20	May 31, '20	Jun 7, '20	Jun 14, '20	Jun 21, '20	Jun 28, '20	Jul 5, '20	Jul 12, '20	Jul 19, '20	Jul 26, '20	Aug 2, '20	Aug 9, '20	Aug 16, '20	Aug 23, '20	Aug 30, '20	Sep 6, '20					
W	S	T	F	M	T	S	W	S	T	F	M	T	S	W	S	T	F	M	T	S	W	S	T	F	M	T	S	W	S	T	F	M	T	S	W

PE Pool & Dive Platform Repair and Natatorium Improvements

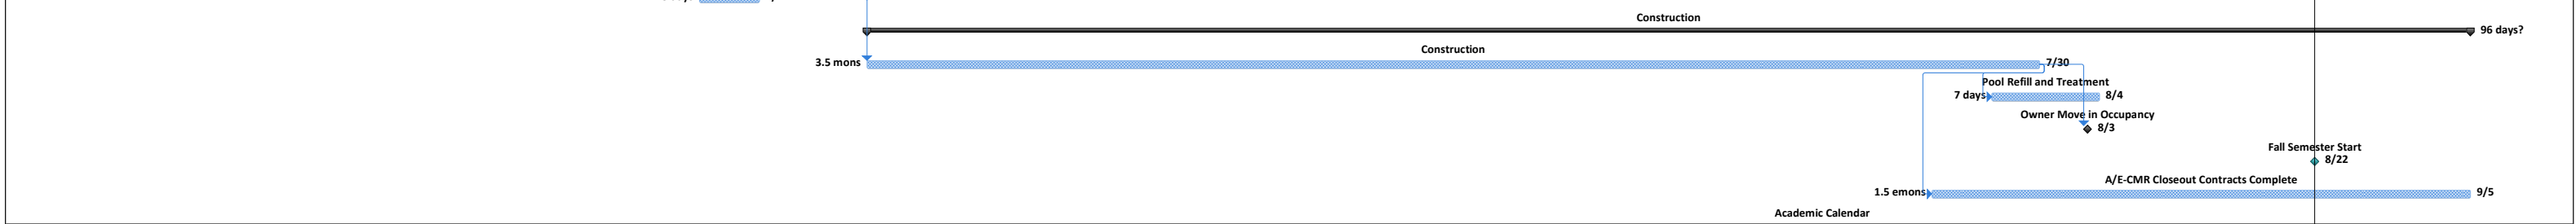

Critical	Critical Progress	Split	Manual Task	Finish-only	Baseline	Baseline Milestone	Summary Progress	Manual Summary	External Tasks	Inactive Task	Inactive Summary
Critical Split	Task	Task Progress	Start-only	Duration-only	Baseline Split	Milestone	Summary	Project Summary	External Milestone	Inactive Milestone	Deadline
